



Bruce Highway Targeted Safety Program

Adam Williams

Program Director (Delivery
Integration)

Building a safer Bruce



\$9 billion for new safety works under the 80:20 joint funding arrangement



Accelerated delivery




Prioritising sections with high safety risk to combat crashes



BHTSP – Achievements

- Single largest safety focused investment
- Program-wide procurement panels are operational
- Established program-specific Principal Arranged Insurance (PAI) Scheme
- Published Program Notes to ensure consistency for project design and delivery

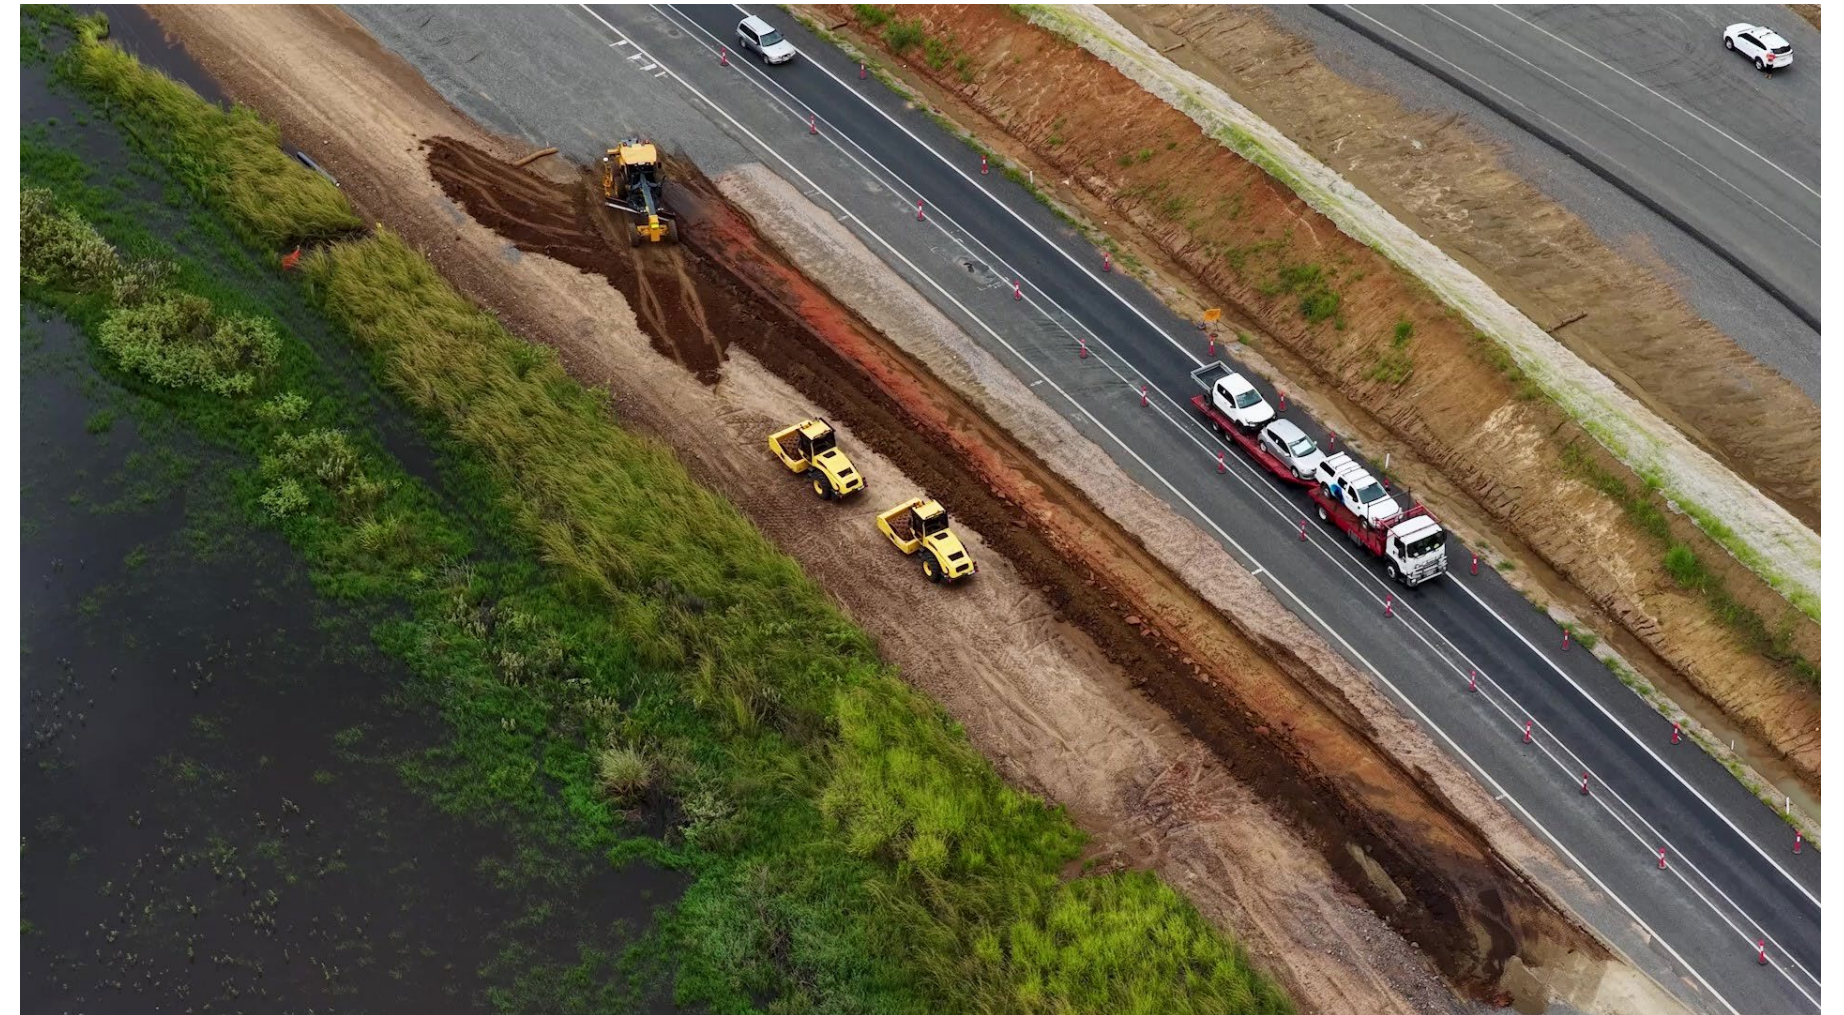

Bruce Highway, Charnwood Rd to Granite Creek, pavement strengthening.

BHTSP – Delivery highlights


- Early start and accelerated works –16 of 38 construction projects already complete
- Baseline Program established – June 2026
- Works to Tender at 30 June 2026 – 5 construction, 17 design (17 released)
- Tender Lookahead Report (2026–27) – 40 construction, 12 design (6 released)
- And more to come



The new Curra Rest Area, north of Gympie.

BHTSP – Procurement

- Industry engagement undertaken in April 2025
- Process to develop panels was launched in August 2025 and finalised in early 2026
- First tender under the new panel arrangement was released in March 2026
- Forward works pipeline outlined in *BHTSP Proposed Works to Tender Lookahead Report* published on TMR's website
- Industry collaboration will continue to shape program delivery

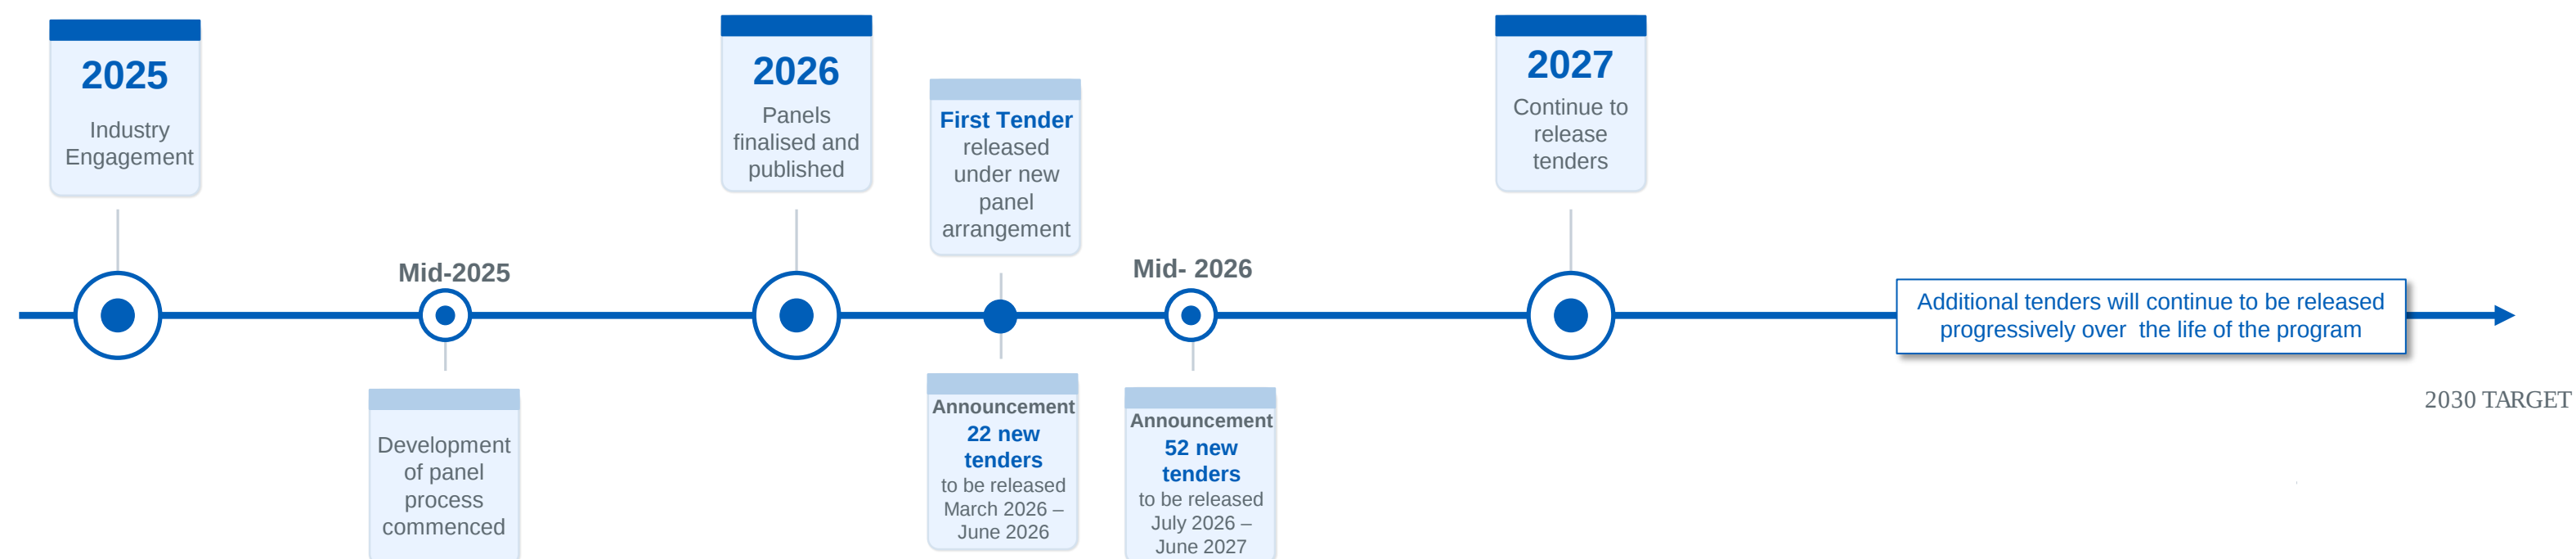

What's next

- Progressive release of tenders
- Increased focus on construction delivery coordination
- Continued focus on safe delivery and effective Temporary Traffic Management
- Shared learnings and working towards increasing delivery efficiency



A section of Bruce Highway near Maryborough.

Thank you and stay connected

www.tmr.qld.gov.au



TMRQld



@TMRQld



@TMRQld



TMRQld



Department of Transport and Main Roads
